

Blackbird Leys Redevelopment

Update: 6th February 2026



Activities completed this week

- **Block D:**
 - Installation of ground floor glazing screens
 - Continuation of internal finishes and snagging
 - Commencement of decorations to communal areas
- **Knights Road:**
 - Phases 1 & 2 - drainage works, services and internal trades continue
 - Phase 3 & 4 – brickwork and internal trades continue
- **Highways:**
 - Soft landscaping preparation
- **Community Centre site**
 - Completion of reduced level dig for foundations
- **Block A**
 - Site logistics works and commencement of piling


Activities planned next week

- **Block D:**
 - External works to continue
 - Internal trades to continue
- **Knights Road:**
 - Phases 1 & 2 – drainage works and internal trades continuing
 - Phases 3 & 4 – brickwork and internal trades continuing
- **Community Centre site**
 - Drainage works
- **Highways works**
 - Soft landscaping preparation
- **Block A**
 - Piling works to continue
 - Continue with hoarding

Knights Road



Chestnut Tower (Block D)

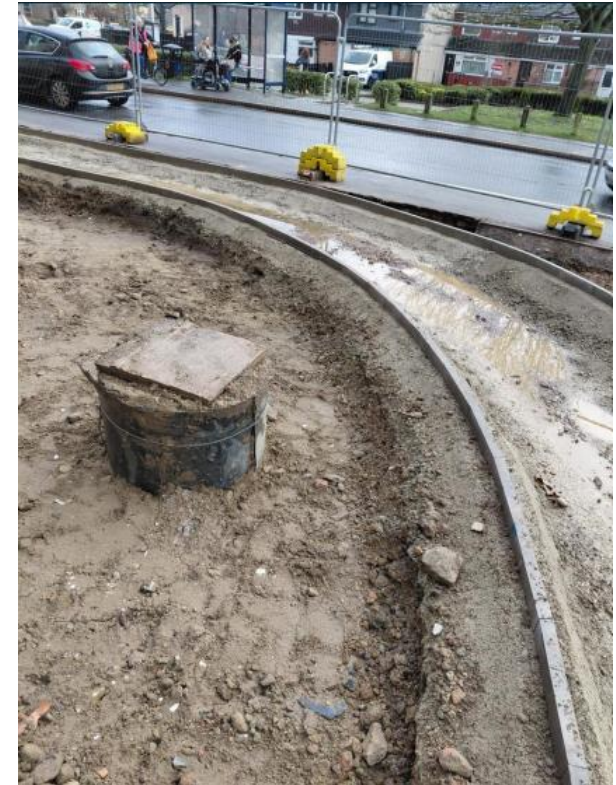

Block A Piling and Community Centre

