

Blackbird Leys Redevelopment

Update: 28th November 2025



Activities completed this week

- **Block D:**
 - Scaffolding removed down to level 2
 - Decorations, mastic, balconies and internal trades
 - Site cabins removed
- **Knights Road:**
 - Phase 1 - Landscaping and inspections
 - Phase 2 - 2nd fix and decorating
 - Phase 3 - Brickwork, roofing and internal trades
 - Phase 4 - Brickwork, foundations and drainage
- **Highways:**
 - Kerbs and new drainage set out
 - Completed drainage in front of shops
- **Community Centre site**
 - Preparation for demolition works




Activities planned next week

- **Block D:**
 - Continue with scaffolding removal, balcony installation and various internal trades
 - Tower crane to be removed on 3rd December (subject to weather)
 - Some hoarding may be removed for external works to start
- **Knights Road:**
 - Phases 1 & 2 – inspections. 2nd fix and final trades to continue
 - Phases 3 & 4 – foundations, drainage, brickwork, roofing and internal trades
- **Highway works**
 - Continue with kerbs and drainage
 - Electrical diversion
- **Community Centre site**
 - Internal demolition works to start


Knights Road



Chestnut Tower (Block D)

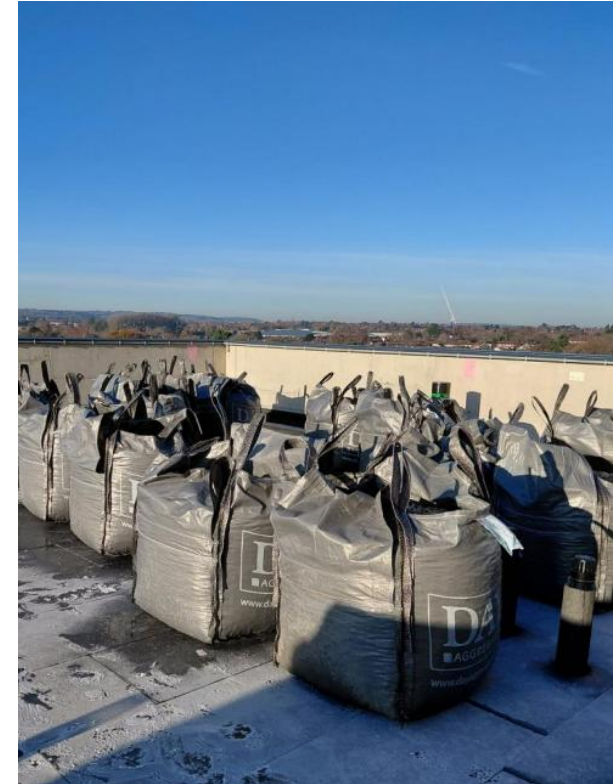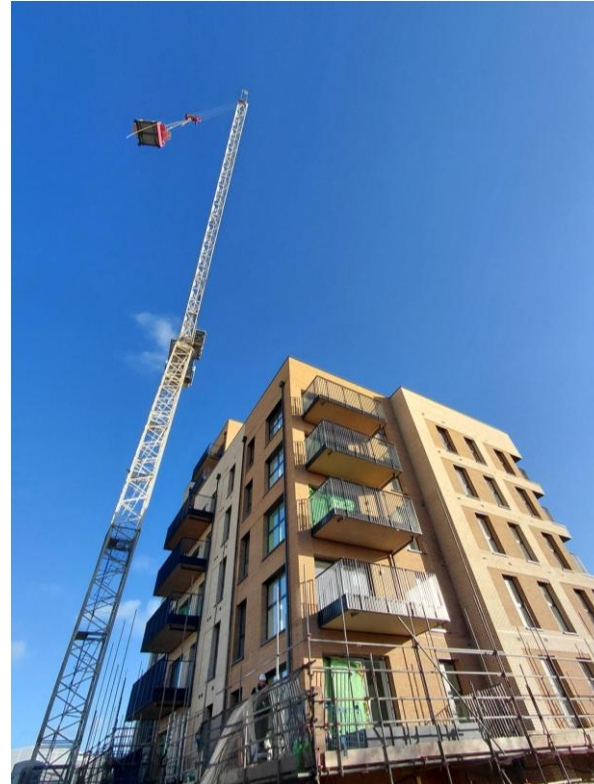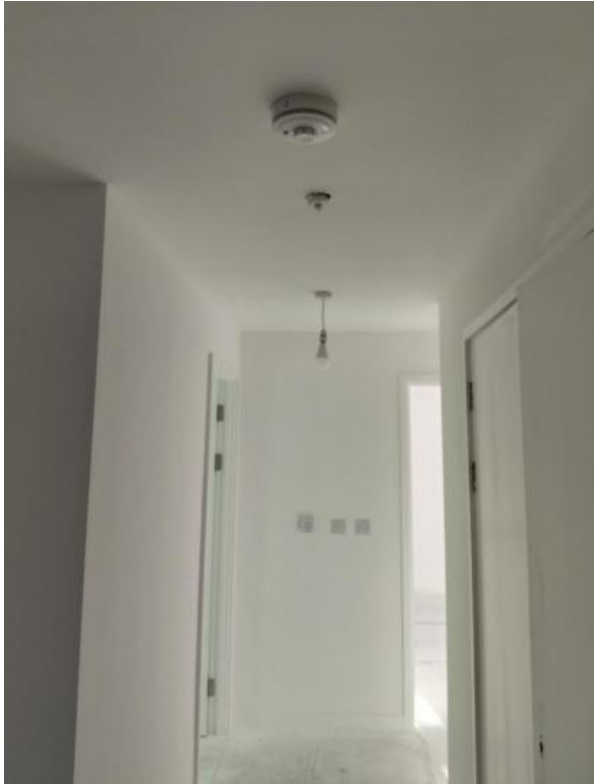

Highways works

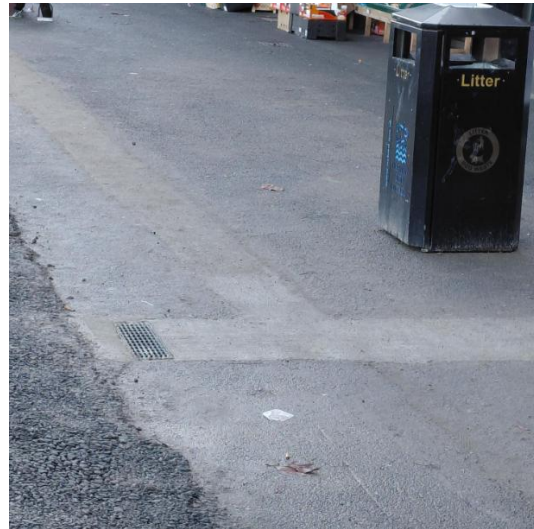

Community Centre

