

Blackbird Leys Redevelopment

Update: 2nd October 2026





Activities completed this week

- **Knights Road:**
 - Handovers
 - Internal trades – painting, carpentry and plumbing
 - External works – fencing, brick walls, forming fronts and capping to sheet piling
- **Community Centre site**
 - Roof waterproofing progressed
 - Steel framing completed on 2nd floor
- **Block A**
 - Core to level 9 completed and level 10 started
 - Halo completed
 - Level 6 – roof pour complete
 - Level 5 – reinforcement in preparation for concrete pour
 - Internal blockwork on ground floor
 - Steel framing commenced on 1st floor


Activities planned next week

- **Block A**
 - Complete core to level 10
 - Level 5 – complete concrete pour
 - Continue internal blockwork on ground floor
 - Temporary waterproofing to podium level
 - Continue steel framing
 - Ground floor waterproofing
- **Knights Road:**
 - External trades – forming gardens, paving and capping to sheet piling
 - Internal trades – painting, carpentry, plumbing and flooring
- **Community Centre site**
 - Continue roof waterproofing
 - Start concrete boarding on 2nd floor
 - Start ground level waterproofing

Community Centre

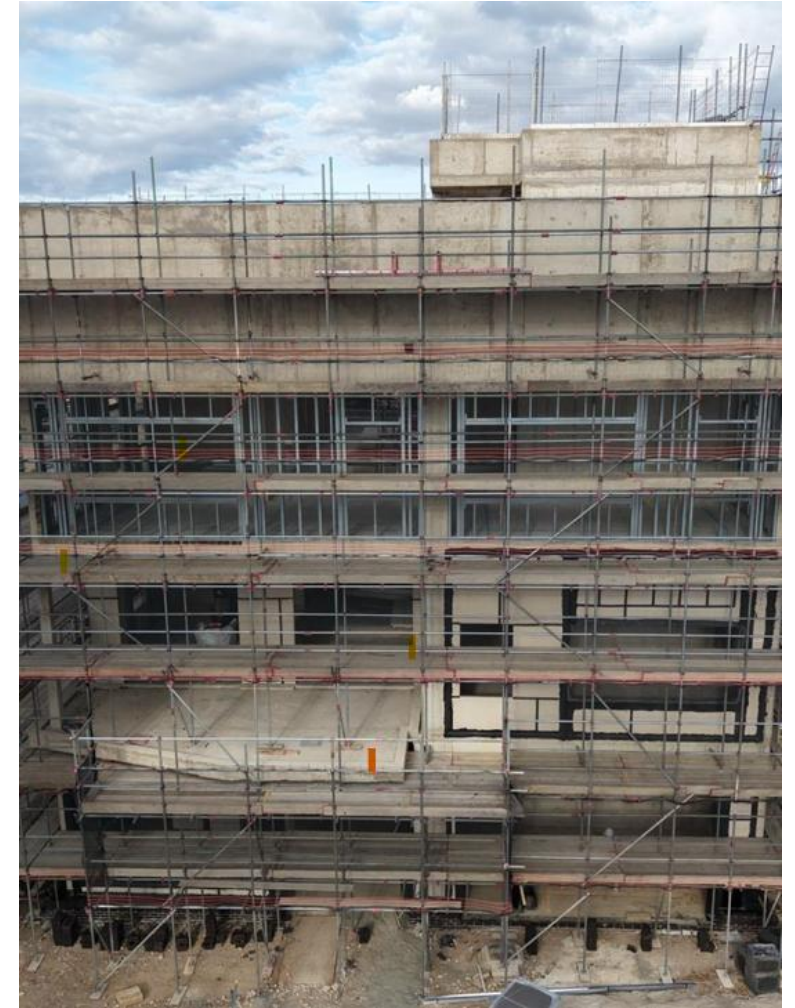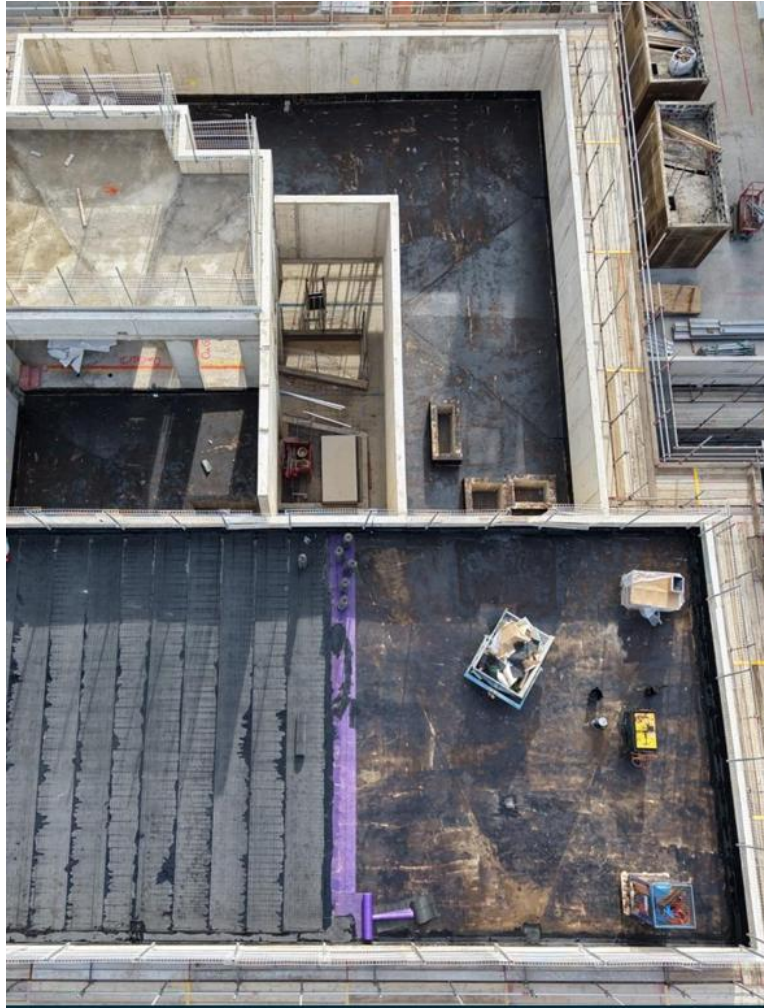

Block A

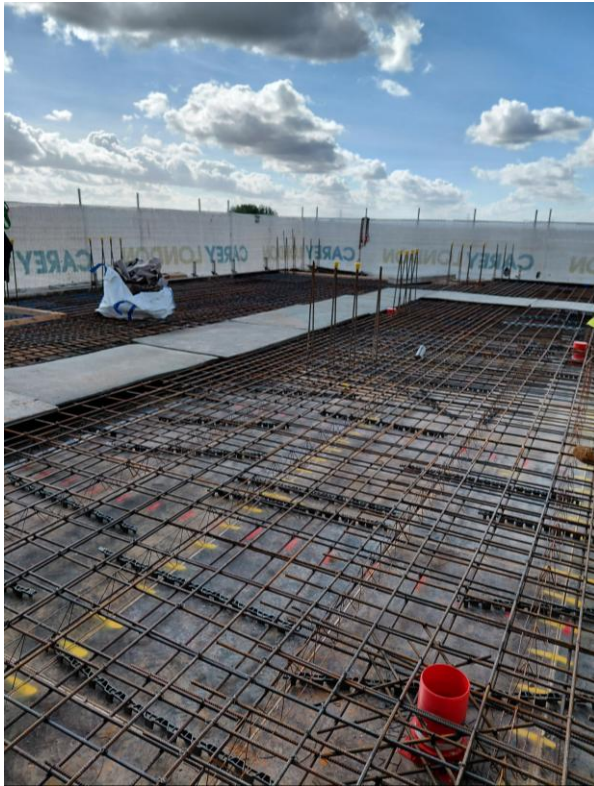

Knights Road

