

# Blackbird Leys Redevelopment

Update: 12<sup>th</sup> June 2026

+

•

○


## Activities completed this week

- **Block D:**
  - New footpaths and cycle paths
  - Commissioning and quality inspections
- **Knights Road:**
  - Phase 2 - External works and internal finishing trades
  - Phase 3 & 4 – Internal and external works
- **Community Centre site**
  - Ground floor decking has been struck
  - 1<sup>st</sup> floor - concrete slab poured
  - Vertical columns to be formed
- **Block A**
  - 100 cubic metres of concrete for ground floor slab
  - Core level 1 reinforcement in progress
  - Ground floor columns started

## Activities planned next week

- **Block D:**
  - Commissioning
  - Complete external works
- **Knights Road:**
  - Phase 2 – handovers, external works and inspections
  - Phases 3 & 4 – external works / internal trades
- **Community Centre site**
  - Level 2 ring beam to be poured
  - Level 2 slabs being delivered and installed
- **Block A**
  - Complete ground floor slab concrete pour
  - Ground floor reinforcement to continue
  - Core level 1 – reinforcement in progress

# Community Centre

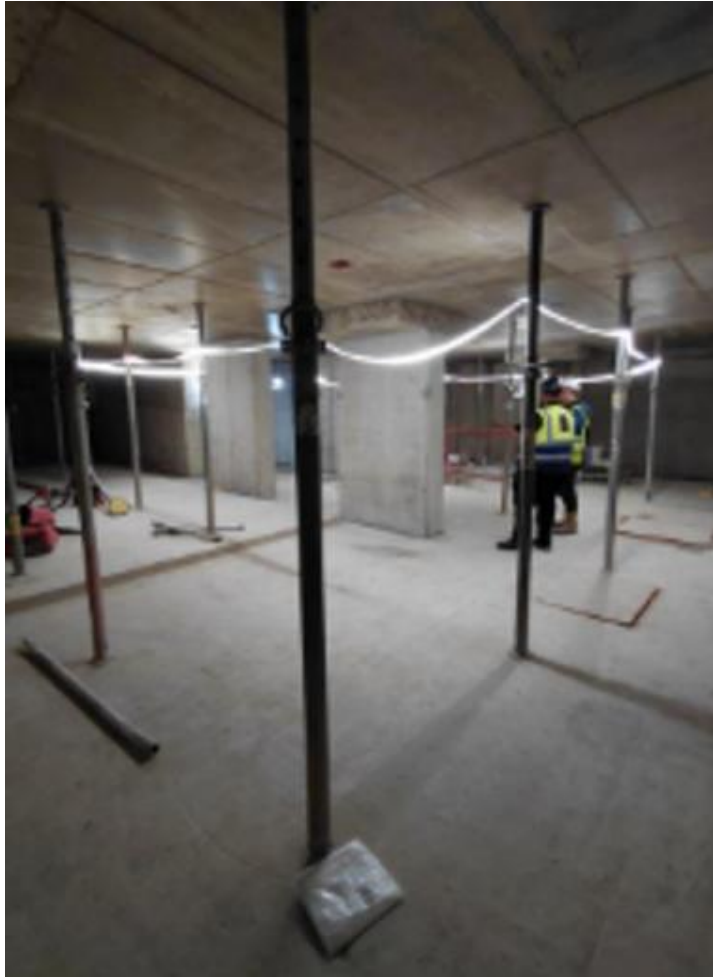

# Knights Road



# Chestnut Tower (Block D)



# Cherry Tree Tower (Block A)

