Blackbird Leys Redevelopment

Update: 24th October 2025

+

0

Activities completed this week

Block D:

- 1st and 2nd fix trades, fire stopping work, and external trades (brickwork, window cills, rainwater pipes)
- Scaffolding removed down another level

• Knights Road:

- Phase 1 planting, fencing and inspections
- Phase 2 Internal works and brickwork
- Phase 3 Brickwork, roofing and internal trades
- Phase 4 Brickwork

Highways:

• Preparation for tarmac - approximately 400 tonnes arrived on Friday!

Activities planned next week

Block D:

- Internal trades continuing including decorating, ceillig
- External trades and scaffolding strike all to continue

Knights Road:


- Phase 1 External trades / inspections
- Phase 2 —Internal trades
- Phase 3 Brickwork, roofing and 1st fix
- Phase 4 Brickwork

Highway works

Complete tarmac. When the tarmac is completed, Blackbird Leys
Road will re-open on 2 way lights



Chestnut Tower (Block D)

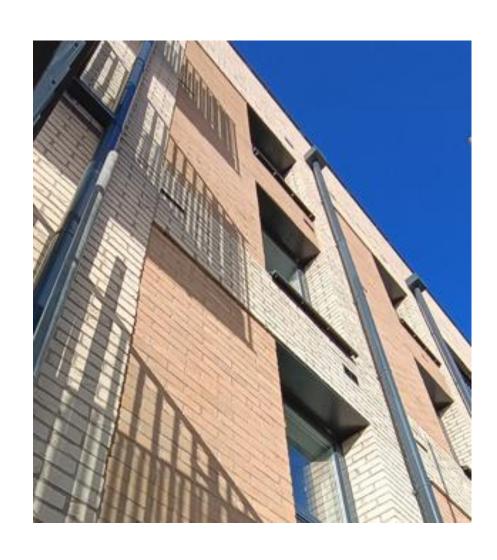



Highways works



