

Blackbird Leys Redevelopment

Update: 14th May 2026

+

•

○

Activities completed this week

Block D:

- External works and landscaping
- Internal trades, commissioning & quality inspections
- Play area – fencing and landscaping

Knights Road:

- Phase 2 - quality inspections / external works
- Phase 3 & 4 – sheet piling / internal and external works

Community Centre site

- Concrete pour to columns

Block A

- Reinforcement for ground beams and retaining walls
- Backfill around basement

Highways

- Works outside Jake's/Nash's

Activities planned next week

Block D:

- Internal trades, commissioning and inspections
- External works and landscaping
- Complete works to play area

Knights Road:

- Phase 2 – finishing trades internally and external works
- Phases 3 & 4 – external works / internal trades

Community Centre site

- Preparing columns & walls for concrete pour


Block A

- Reinforcement for ground beams / retaining walls
- Concrete pour for basement walls

Highways

- Complete footpath and handrail outside Jake's/Nash's

Community Centre

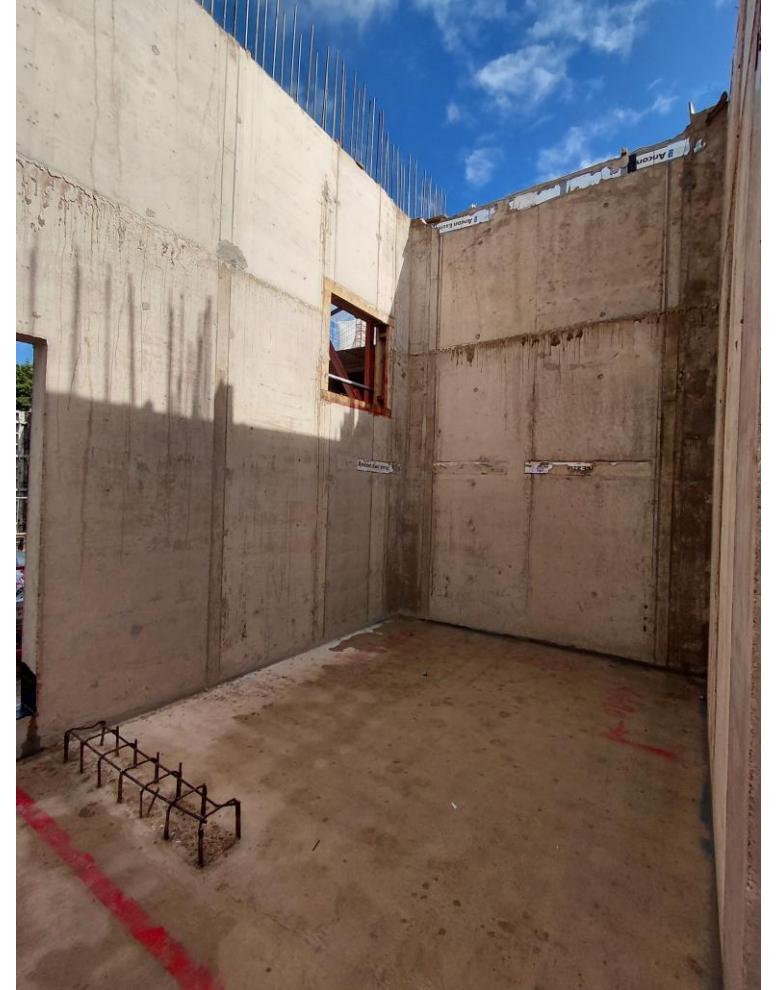

Knights Road



Chestnut Tower (Block D)



Cherry Tree Tower (Block A)

