

Blackbird Leys Redevelopment

Update: 27th February 2026

+

•

○

Activities completed this week

- **Block D:**
 - External works – parking, cycle lane and footpath
 - Internal trades and quality inspections
- **Knights Road:**
 - Phases 1 & 2 - internal trades, fencing & drainage
 - Phase 3 & 4 – brickwork and internal trades
- **Highways:**
 - Soft landscaping – turfing and trees
- **Community Centre site**
 - Reduced level dig
 - Groundbreaking event
- **Block A**
 - Piling works
 - Crane base completed

Activities planned next week

- **Block D:**
 - External works to continue
 - Internal trades – decorating and flooring & electrical
- **Knights Road:**
 - Phases 1 & 2 – drainage works and internal / external works and handovers
 - Phases 3 & 4 – brickwork and internal trades continuing
- **Community Centre site**
 - Retaining walls to be built
- **Highways works**
 - Landscaping to continue
- **Block A**
 - Piling works to continue
 - Currently programmed and rig to be removed by the end of next week




Community Centre



Knights Road



Chestnut Tower (Block D)

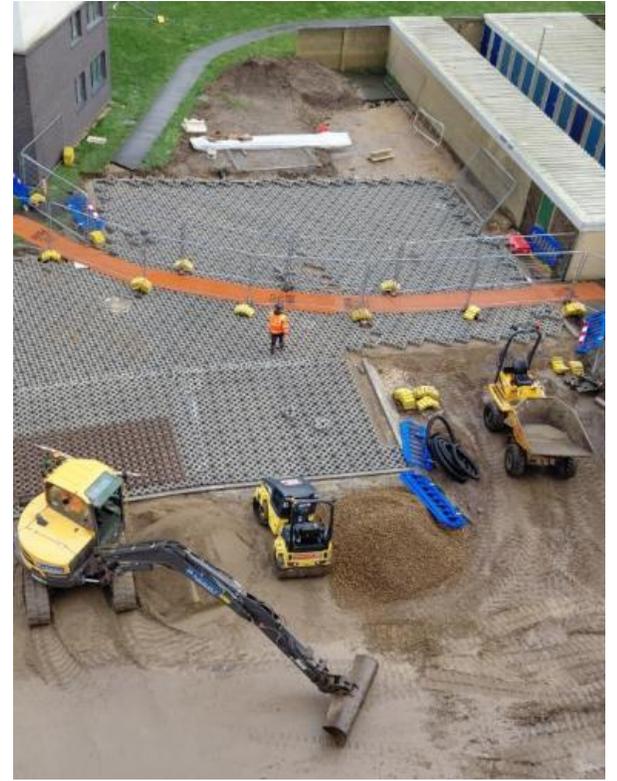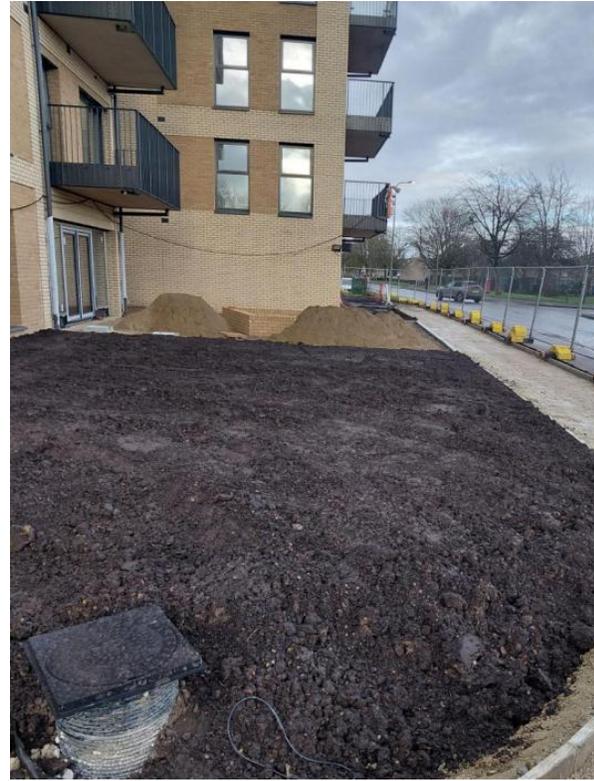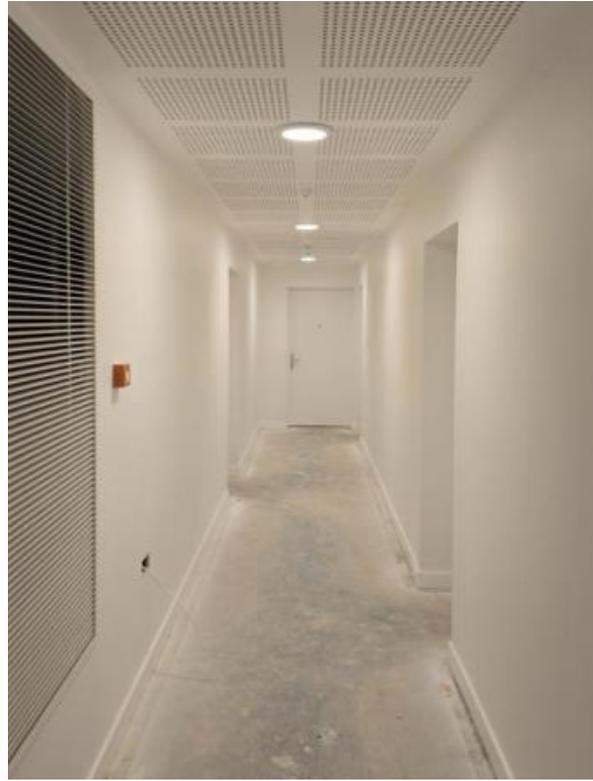

Block A



Highways

