

Blackbird Leys Redevelopment

Update: 20th February 2026

+

•

○

Activities completed this week

- **Block D:**
 - External works
 - Internal trades continued and quality inspections
- **Knights Road:**
 - Phases 1 & 2 - drainage works, internal trades and fencing
 - Phase 3 & 4 – brickwork and internal trades
- **Highways:**
 - Soft landscaping – turfing and trees
- **Community Centre site**
 - Reduced level dig
- **Block A**
 - Piling works
 - Crane base started


Activities planned next week

- **Block D:**
 - External works to continue
 - Internal trades – decorating and flooring & electrical
- **Knights Road:**
 - Phases 1 & 2 – drainage works and internal and external works
 - Phases 3 & 4 – brickwork and internal trades continuing
- **Community Centre site**
 - Foundations to start
- **Highways works**
 - Landscaping to continue
- **Block A**
 - Piling works to continue. Currently programmed to complete on 27th February
 - Complete crane base

Knights Road



Chestnut Tower (Block D)

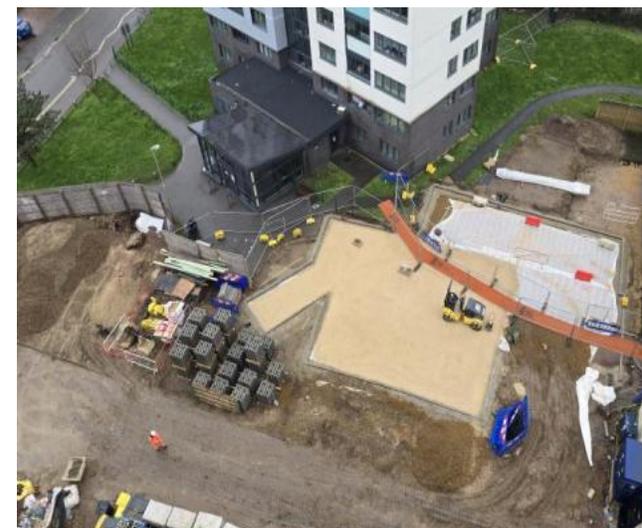

Highways



Block A



Community Centre

