

Blackbird Leys Redevelopment

Update: 17th April 2025

+

•

○

Activities completed this week

Block D:

- Steel framing, window installation, internal partitions , mechanical systems installations on – going throughout the block
- Roofing works and brickwork started
- Hoarding changed around Block D

Highways:

- Service diversions and street lighting
- Raised crossing works near Evenlode Tower

Knights Road:

- Phase 1 – internal and external works and excavations for services
- Phases 2a and 2b - general groundworks / foundations / brickwork and scaffolding
- Phase 3 – piling works started

Activities planned in next 2 weeks

Block D:

- Continue steel framing, window installation, internal partitions and mechanical systems works, brickwork, roofing works, screeding and brickwork


Knights Road:

- Phase 1 – continue with internal and external works
- Phases 2a and 2b – brickwork to continue
- Phase 3 – piling works to complete


Highways works

- Road closure extended to 9th May.
- Re-surfacing to be carried out beginning of May.
- Continue service diversions, forming roads, footpaths and street lighting
- 3 - way lights by Windrush Tower for 1 week – subject to Thames Water attending

Knights Road

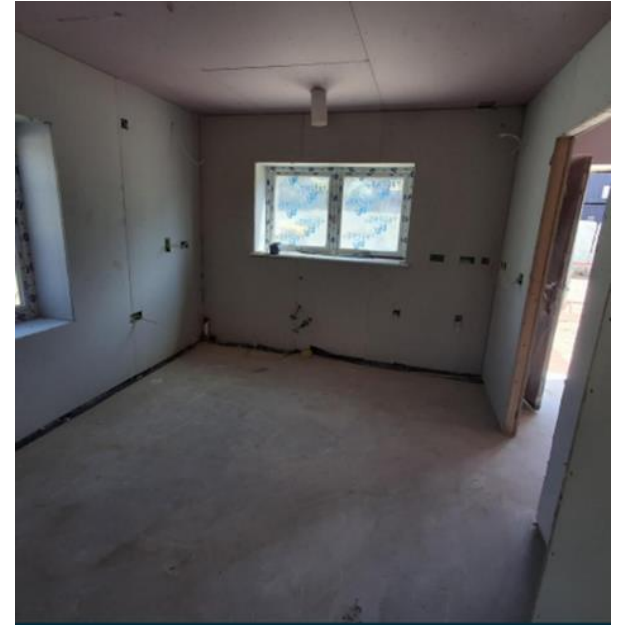

Block D

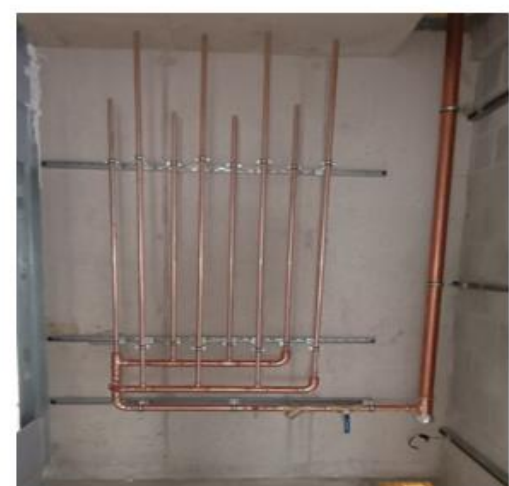

Highways works

